AOC-WebAPI — WBSO 2026 Status and Plan

Oct 14, 2026 · @Filippo

Summary

The project is on track to close by 31 December 2026: TC1 and TC2 are complete, TC3 and TC4 are delivered with documented deviations, and TC5 is in progress for October–November.

- **Project:** SW2 — AI-Driven Agentic Orchestration Software (AOC-WebAPI), development project, 1 January – 31 December 2026, 1,150 approved hours.
- **Hours:** 908 hours registered through mid-October (79%); about 242 hours remain, in line with the monthly pace so far.
- **Demonstrator:** a read-only, audited repository-diagnostics workflow. It passes 9 of 9 checked-in cases with recovery enabled and 7 of 9 without it, and every run replays from signed evidence without repository or tool access.

Progress per technical challenge

All five components from the application exist in working form; the open R&D work is concentrated in TC5.

Challenge	Committed in application	Delivered (as of 14 Oct)	Status
TC1 Deterministic execution	Seed-locked, time-boxed runs; HMAC event logs; signed manifests; byte-identical replay	All delivered; 16 signed golden scenarios replay identically; tampering is detected	Complete; replay speed to be measured in November
TC2 Capability router	Latency/cost/quality/compliance scoring, historical weighting, decision within 10 ms	All delivered; stable decisions; p95 well below 10 ms on the current catalog	Complete; scaling test with more conditions in November

Challenge	Committed in application	Delivered (as of 14 Oct)	Status
TC3 Secure sandbox	Pre-warmed gVisor/Firecracker isolation, memory-mapped injection, JWT tokens, under 50 ms	Pre-warmed hardened containers, JWT per tool call, tenant-separation tests; warm p95 26.7 ms, cold p95 225 ms	Delivered with deviations (see below)
TC4 Planning with local <7B models	Hierarchical plans, semantic playbooks, step validation, recovery	Playbooks, validated plans, critic, one-step recovery; success on recoverable cases 0/2 to 2/2	Delivered with deviations; local-model measurement in October
TC5 Evaluation and drift	Exact and semantic scoring, confidence calibration, CUSUM drift detection	Exact golden replay and case scoring	In progress: semantic scoring and calibration in October, CUSUM in November


Deviations from the application

Four points differ from the application text; each will be reported in the December evidence pack as an experiment result with its reasons.

Area	Application	Actual approach	How it is handled
Isolation runtime (TC3)	gVisor/Firecracker micro-VMs	Hardened OCI/runc containers; the design keeps a slot for a gVisor or micro-VM backend	Optional gVisor trial on a Linux VM; otherwise documented with measured results

Area	Application	Actual approach	How it is handled
Code injection (TC3)	Injection via memory mapping	Not implemented; pre-warming used instead	Documented as an evaluated approach; warm path meets 50 ms, cold path does not
Planning (TC4)	Hierarchical plans from local <7B models, semantic playbooks	Single-level plans from deterministic playbooks with exact term retrieval; April trial showed raw local-model plans were unreliable	Measure a local model on the same cases in October; report the result either way
Tooling	ONNX Runtime, Semantic Kernel baseline, Redis/MinIO, MathNet.Numerics	Not used so far	MathNet.Numerics planned for CUSUM/calibration; a small Semantic Kernel replay baseline if time allows

Plan to year end

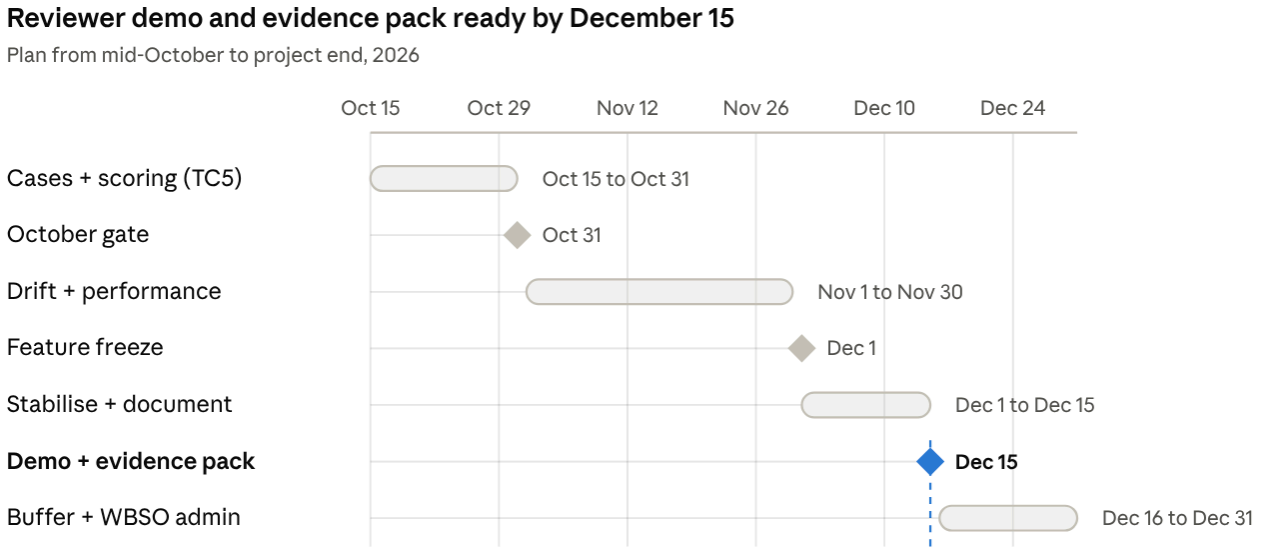


project plan and October status · 14 October 2026

Features freeze on 1 December so that the demo, documentation and evidence pack are ready by 15 December, leaving the rest of December as buffer.

- **By 31 October:** three remaining diagnostic cases, exact and semantic scoring, confidence calibration, a per-stage regression report, and a measured local-model comparison. Gate: at least 10 of 12 cases succeed, with 100% allowed-action validity, prohibited-action rejection and replay equivalence.
- **November:** CUSUM drift detection, replay-speed and router-scaling measurements, repeated and concurrent runs, and a demo on a frozen snapshot of the project's own repository.
- **By 15 December:** a scripted demo showing a correct diagnosis, a recovered failure, a denied unsafe request and an identical replay, plus the WBSO evidence pack and final TC1–TC5 conclusions.

Hours and administration

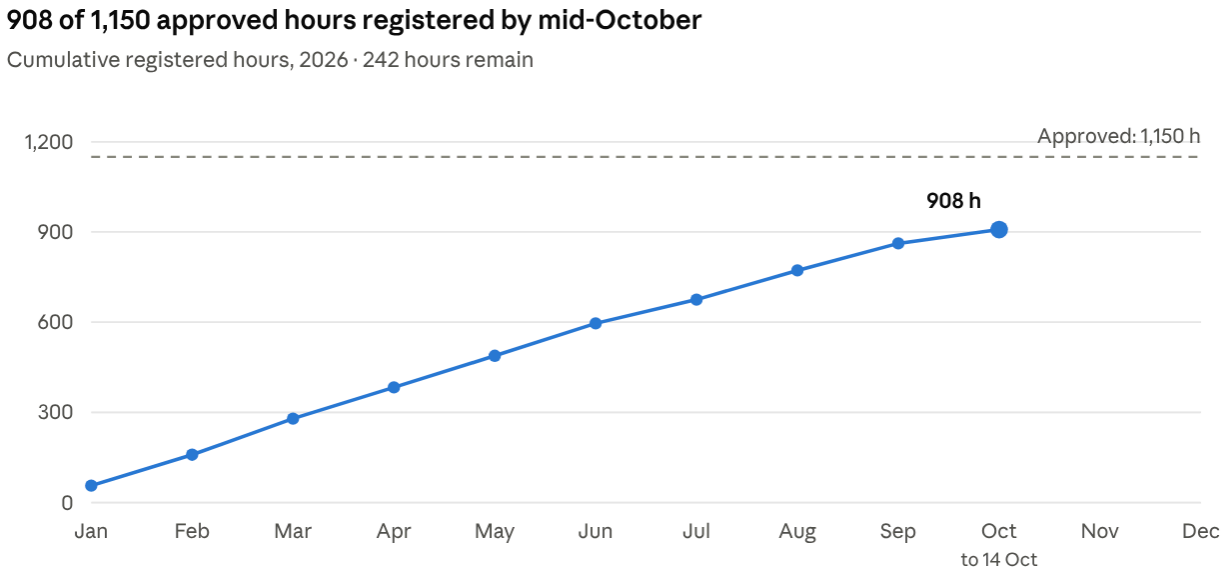

WBSO hours registration, overview sheet · January to 14 October 2026

January to September averaged about 96 hours a month; the remaining 242 hours over the rest of the year need about the same pace.

- Hours are recorded per month in the registration workbook and must be updated at least every 10 working days.
- The Q3 project administration is due by the end of November 2026.
- Technical evidence is kept in the repository: a dated deliverable per month and a TC1–TC5 evidence file that maps each challenge to experiments, tests and measurements.
- To correct: the May sheet has an invalid value in its Year cell.
